



STRIVE Global — Full HubSpot CRM Overhaul Proposal

A comprehensive two-phase CRM transformation to fix pipeline visibility, automate board reporting, and unlock the HubSpot Enterprise investment STRIVE is already paying for.

PREPARED BY SAYER

CONFIDENTIAL

A Note on This Proposal

Proposals are inherently a starting point — not a final blueprint. This document reflects our understanding of your challenges, a proposed solution, and the resources required to execute successfully.

We recognize that you, as the client, live with these challenges daily, and there may be details we have yet to uncover. Our goal is to use this as a conversation starter — to refine, align, and ensure we are solving the right problems in the right order.

If any aspect of the scope, solution, or pricing feels misaligned, let's use that as a basis for further discussion.

Our Commitment

This proposal is a living document. We are committed to refining the scope, solution, and investment until it is exactly right for STRIVE Global.

- Transparent communication throughout
- Flexible phasing to match your priorities
- ROI-first approach to every decision

Executive Summary

STRIVE Global is a PE-backed (Essex Bay Capital) benefits technology company headquartered in Denver, CO with approximately 51 employees. STRIVE offers white-labeled employee benefits apps, AI-powered benefits assistants, scalable microsites, and a rewards platform (Divi) distributed through a broker channel model. Sales motions range from **\$6K client-level deals to \$400K+ enterprise broker packs.**

Phase 1: CRM Foundation Weeks 1–8 Pipeline restructuring, contact classification, deal health scoring, automated board dashboards, data normalization, and parent-child broker structures.	Phase 2: CPQ, Enrichment & Integrations Weeks 9–18 CPQ implementation, AI-powered data enrichment at scale, email sequencing, marketing automation, commission visibility, and integration preparation for NetSuite and Bill.com.	Why Phased? Risk-Managed Approach STRIVE’s data quality issues make it risky to build CPQ on unclassified contacts. Phase 1 creates the clean foundation Phase 2 depends on — with a natural board checkpoint between them.
--	---	--

THE CHALLENGE

The Problem

After 10 years of organic growth, STRIVE's HubSpot instance has become a bottleneck — not an asset.

120+ hours/year

Spent on manual board report preparation. Andrea spends 1+ full business day every month assembling reports by hand.

Zero Contact Classification

10 years of contact records with no way to distinguish clients from prospects from brokers from partners.

Pipeline Under-Reported

Deals are quoted manually outside the CRM. They never enter the pipeline. The board sees an incomplete picture.

Gut-Feel Forecasting

No probability weighting, no deal health scoring, no objective pipeline reviews. Forecasting is entirely subjective.

Reps Default to LinkedIn

CRM data is unreliable, so reps work in LinkedIn Sales Navigator. Activity is never logged. Institutional knowledge is lost.

📌 This is not a technology problem. It is a **data infrastructure problem** that compounds every quarter as the team scales.

Objectives

Fourteen clearly defined outcomes across both phases — each tied to a measurable business result.

01

Separate Pre-Pipeline from Active Pipeline

Eliminate metric distortion and enable accurate forecasting

03

Implement Deal Health Scoring

Replace gut-feel forecasting with objective pipeline reviews

05

Implement HubSpot CPQ

Complete product library, quote templates, e-signatures, and automated reminders

07

Deploy AI-Powered Data Enrichment

Auto-classify and enrich the full database at scale

- **Launch Email Sequencing**
Broker prospecting and client expansion outreach
- **Build Marketing Automation Foundation**
Newsletter templates and segmented campaigns
- **Prepare for NetSuite & Bill.com Integration**
Data readiness and field mapping (prep only)
- **Optimize Seat/License Allocation**
Reduce unnecessary subscription costs
- **Implement Commission Visibility**
Validation workflow tied to closed-won deals
- **Standardize Data Entry**
Close won/lost reasons, lead source tracking, required fields

02

Classify All Contacts by Type

Using AI enrichment to unlock segmented marketing and targeted outreach

04

Automate Board Dashboards

Eliminate 8–10 hours/month of manual report assembly

06

Build Contract Management Workflows

Replace the manual DocuSign process through the COO

08

Establish Parent-Child Broker Structures

Enable microsite-to-app expansion prospecting

PHASE 1

Phase 1: CRM Foundation (Weeks 1–8)

Phase 1 delivers the highest-impact fixes first: pipeline clarity, contact classification, board dashboards, and deal health scoring. It pays for itself independently and can stand alone as a complete engagement.



CRM Architecture & Config Review — 12 hrs

Portal audit, user roles, permissions, team structure reconfiguration, seat/license review across 3 hubs.



Pipeline Restructuring — 24 hrs

Pre-pipeline separation, partner/client deal categories, stage probability mapping (5/20/40/50/60/80/90/100), Contracting stage, required fields, auto-transitions with deal age reset.



Contact & Company Classification + Cleanup — 24 hrs

Contact type taxonomy (client/prospect/broker/partner), AI enrichment pilot on 500 records, full database classification, normalization, deduplication, association fixes, duplicate protection.



Deal Health Scoring & Forecasting — 10 hrs

Deal score formula (stage + time-in-stage + activity recency), healthy/at-risk/stale classification, standardized close won/lost reason dropdowns.

Phase 1: Data, Reporting & Training

Data Normalization & Dedup — 14 hrs

Full database normalization (capitalization, phone formats, addresses), advanced deduplication with configurable matching rules, merge strategy, ongoing duplicate protection.

Parent-Child Structure (Broker Packs) — 8 hrs

Company-to-company association labels, per-broker intake forms in HubSpot CMS, automated child contact creation, segmented lists by parent broker for expansion prospecting.

Automations & Workflows — 14 hrs

Outlook email logging fix, lead source tracking, form-to-CRM automation, stage-change notifications, duplicate protection, pre-pipeline auto-transition. Up to 10 workflows.

Reporting & Dashboards — 20 hrs

Partner, seller, CEO/board, and pipeline health dashboards. Up to 15 custom reports with scheduled exports.

Email & Communication Fix — 6 hrs

Outlook integration audit, association rule configuration, domain exclusions.

Training (Admin, End Users, Executive) — 17 hrs

1–2 admin sessions, 2–3 end-user sessions, 1 executive session. All virtual and recorded for future onboarding.

UAT, Go-Live & Documentation — 10 hrs

Test scripts, 2 UAT sessions, bug fix window, admin + user guide, 2-week hypercare.

Project Management — 18 hrs

Kickoff, weekly syncs, status updates, milestone reviews, scope creep prevention.

📌 **Phase 1 Total: 177 median hours | \$26,550**

PHASE 2

Phase 2: CPQ, Enrichment & Integrations (Weeks 9–18)

Phase 2 builds on the clean foundation with quoting automation, AI-powered enrichment at scale, marketing automation, and integration preparation. Each workstream depends on Phase 1 data quality.

66
99

CPQ Implementation — 45 hrs

Complete product library (apps, microsites, AI assistant, broker packs, Divi/rewards, bundles). Multiple pricing models (license + rev share, flat per-head, bundle discounts). Branded quote templates, e-signatures, automated reminders, quote-to-deal automation. Industry benchmark: 40–60 hours for CPQ rollout.



Contract Management Workflows — 11 hrs

Quote-to-contract automation, contract status tracking, renewal/expiry notifications, auto-advance on signature. Replaces manual DocuSign process through COO.



Data Enrichment at Scale — 12 hrs

Full database Breeze AI enrichment (extends Phase 1 pilot), auto-enrichment for new inbound contacts, QA and validation, accuracy documentation.



Email Sequencing — 8 hrs

Broker prospecting sequence, microsite-to-app expansion sequence, up to 4 total sequences with enrollment triggers and performance reporting.

Phase 2: Marketing, Integrations & Reporting

Marketing Automation Foundation — 11 hrs

Newsletter template branded to STRIVE, 2–3 segmented campaigns by contact type, unsubscribe management and CAN-SPAM compliance, campaign performance reporting. Leverages Marketing Hub already licensed.

Commission Visibility & Validation — 6 hrs

CRM-based commission view tied to closed-won deals, validation workflow for Jodi to review and approve before release, summary report by rep and time period. Visibility only — not a full calculation engine.

NetSuite Integration Prep — 11 hrs

Data readiness documentation, field mapping between HubSpot and NetSuite entities, gap analysis, integration readiness report. **PREP ONLY** — actual build requires separate SOW.

Bill.com Integration Prep — 6 hrs

AR/AP field mapping requirements, data readiness assessment, integration readiness report. **PREP ONLY**.

Seat/License Optimization — 3 hrs

Audit all 23 seats across core, sales, and service hubs. Cost savings recommendation with specific seat changes.

Advanced Reporting — 11 hrs

Automated board report delivery (scheduled email), pipeline coverage vs. quota, pace-to-goal reporting, marketing campaign ROI.

Additional Project Management — 16 hrs

Phase 2 PM, weekly syncs, milestone reviews, change request management.

📅 Phase 2 Total: 140 median hours | \$21,000

OPTIONAL ADD-ON

Client Success Pipeline

A Client Success pipeline to track client health, renewals, and billing integration is available as an optional add-on. This workflow requires a separate discovery call with the Client Success team to define requirements and is not included in the base project cost.

11 Median Hours

Estimated scope for the Client Success pipeline workflow, subject to discovery.

\$1,650 Estimated

Add-on investment at the standard \$150/hr rate. Final scope confirmed after discovery call with the Client Success team.


Flexible Timing

This can be added at any point during or after the engagement — no need to decide now.



Timeline

A phased rollout ensuring each phase delivers standalone value with a natural checkpoint between them.

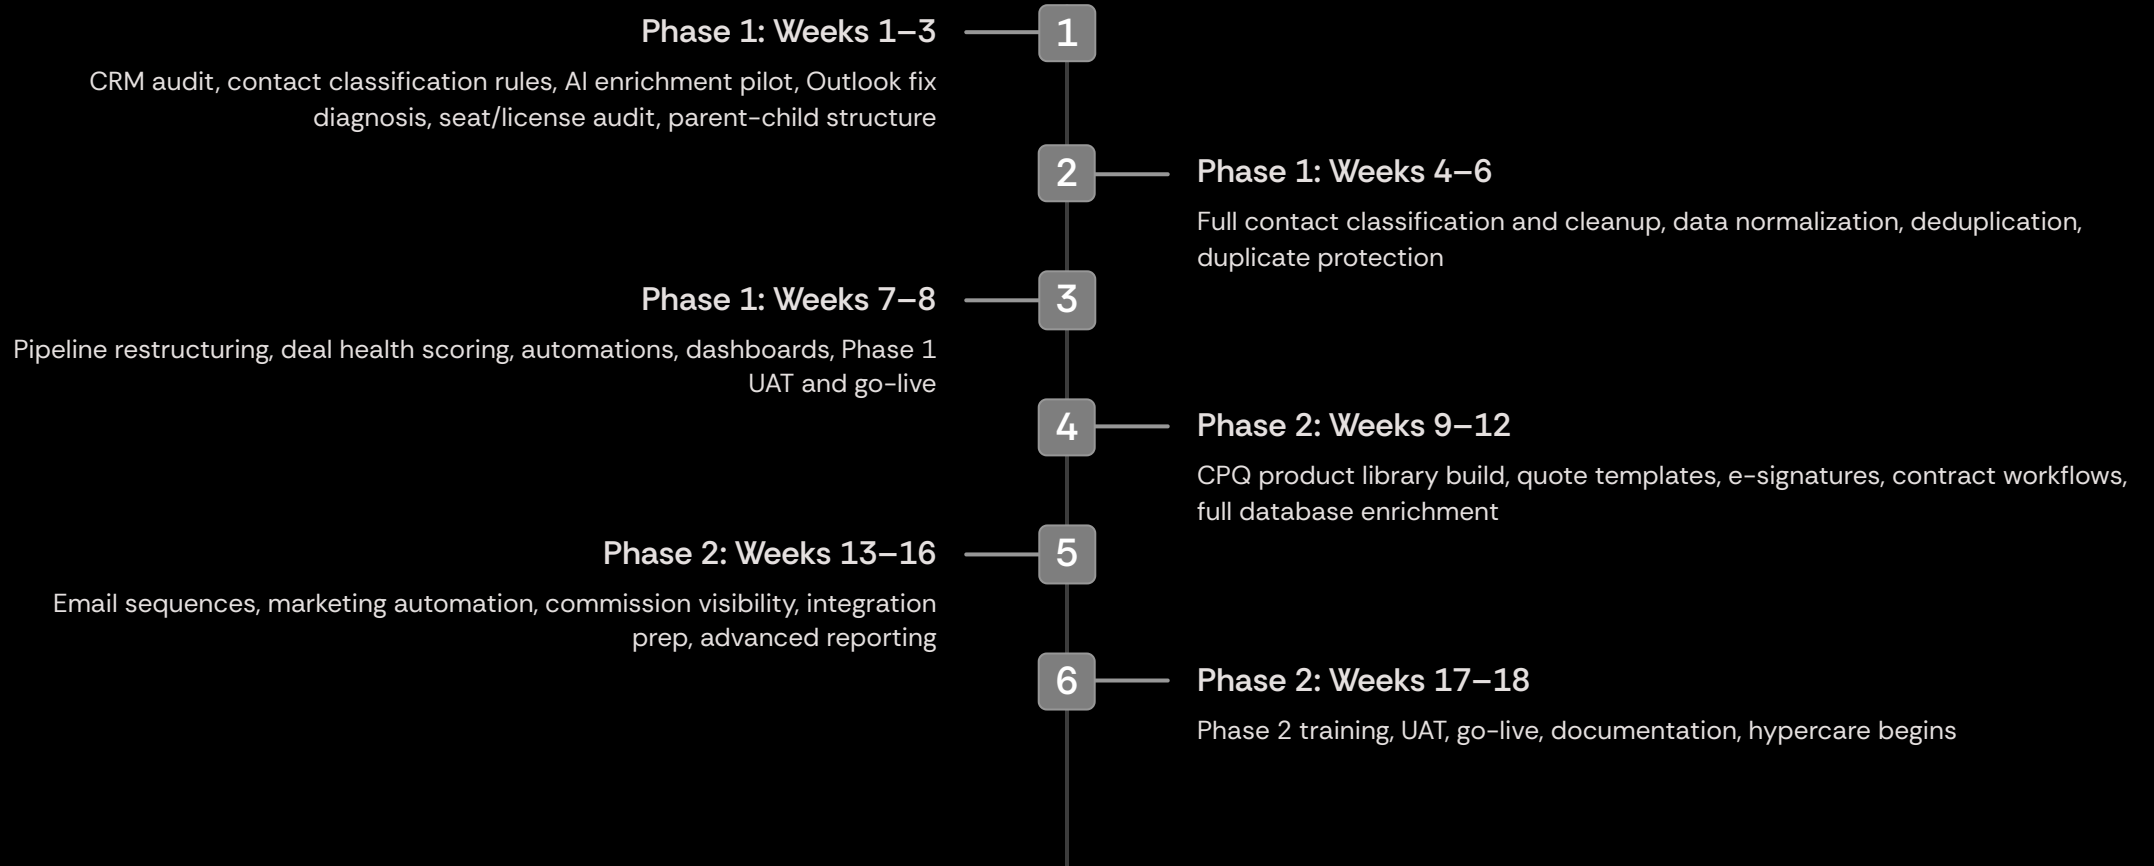

INVESTMENT

Investment

\$46,950

Total Project Investment

Fixed fee at \$150/hr across 313 median hours. No surprises — no hourly overages.

Component	Model	Fee
Phase 1: CRM Foundation (Weeks 1–8)	Fixed Fee	\$26,550
Phase 2: CPQ + Enrichment + Integrations (Weeks 9–18)	Fixed Fee	\$21,000
Project Total	Fixed Fee	\$46,950

Payment Terms

- Phase 1: 50% (\$13,275) at Phase 1 kickoff, 50% (\$13,275) at Phase 1 handoff
- Phase 2: 50% (\$10,500) at Phase 2 kickoff, 50% (\$10,500) at Phase 2 handoff
- Net-15 terms on all invoices

A 5% Technology & Administrative fee is applied to each invoice to offset costs of our technology stack and internal systems.

- 📄 **Budget Flexibility:** Phase 1 can stand alone as a complete engagement at \$26,550. STRIVE can approve Phase 1 only and engage Phase 2 as a separate project after demonstrating Phase 1 ROI to the board.

Project Governance

Sayer Responsibilities

- Lead configuration, QA, and implementation across all workstreams
- Conduct weekly check-ins and milestone reviews
- Provide documentation, training, and go-live support for each phase
- Manage project timeline and proactively communicate risks or blockers
- Deliver ROI tracking framework for post-project measurement
- Produce seat/license optimization memo with cost savings recommendations
- Deliver integration readiness reports for NetSuite and Bill.com

STRIVE Responsibilities

- Designate 1 primary point of contact (Andrea recommended)
- Ensure Jodi and Andrea availability for discovery, UAT, and training
- Provide complete product/pricing inventory before Phase 2 CPQ build
- Provide contact classification rules and validate AI enrichment results
- Confirm deal stage definitions and probability framework
- Share 3–5 recent quotes/proposals across deal types for CPQ reference
- Mandate CRM usage across sales team (executive sponsorship critical)
- Complete UAT testing within agreed timeline for each phase
- Provide full HubSpot admin access

Assumptions & Constraints

✓ In Scope

- HubSpot Sales Hub Enterprise (existing instance — reconfiguration)
- Up to 23 licensed users across core, sales, and service seats
- Outlook as primary email platform
- Up to 40 custom properties (expanded for CPQ and enrichment)
- 1 active sales pipeline with pre-pipeline separated
- 2 deal categories: partner-level and client-level
- AI enrichment using HubSpot Breeze credits (5–10K)
- Up to 12 automated workflows
- 4–5 dashboards with up to 20 custom reports
- 16–18 week phased timeline
- All work conducted remotely

⊘ Out of Scope

- NetSuite / Bill.com integration build (prep only — actual build requires separate SOW)
- Client Success pipeline (available as optional add-on)
- Full commission calculation engine (visibility and validation only)
- Custom API development or middleware beyond HubSpot native
- Data migration from external systems (internal cleanup only)
- Ongoing managed services beyond 2-week hypercare per phase
- HubSpot license procurement or tier changes (recommendations provided)
- AI knowledge assistant for sales onboarding (future initiative)
- LinkedIn Sales Navigator integration (recommended for future)

📌 Any scope changes require formal approval and may impact cost or timing.

NEXT STEPS

Approval & Next Steps

Please confirm alignment on scope and structure so we can move forward with scheduling a formal kickoff and assigning your Sayer team.

1

Written Approval

Provide written approval of this proposal via email — full project or Phase 1 only.

2

Schedule Kickoff

Project kickoff within 1–2 weeks of written approval.

3

Execute MSA

Sayer will issue a Master Services Agreement via DocuSign with this Scope of Work included.

4

Begin Onboarding

Once the MSA is executed, Sayer will finalize the implementation plan and begin onboarding.

📌 This proposal is designed with budget flexibility — Phase 1 can be approved independently with Phase 2 engaged after demonstrating ROI. If any scope areas, phasing, or pricing need to be adjusted, we welcome the conversation.

ROI Appendix

The Story for the Board

"We have a HubSpot Enterprise license that we're paying for but not using. Ten years of data sitting in the CRM with no classification, no forecasting, no automation. Our sales leader spends more than a full day every month building board reports by hand. Deals are quoted in email and never enter the pipeline. We're flying blind.

This investment fixes the foundation. Phase 1 gives us clean data, accurate pipeline reporting, and automated board dashboards within 8 weeks. Phase 2 adds quoting automation, AI-powered data enrichment, and prepares us for NetSuite integration — all using tools we're already paying for.

The investment pays for itself within 6 months through time savings alone. The real return is pipeline visibility, board-ready reporting without manual assembly, and the data infrastructure to scale the sales team and leverage AI.

We're not buying new software. **We're unlocking the software we already own."**

ROI PILLAR 1

Time Savings — \$45,600 – \$77,700/year

Hours that Andrea and Jodi get back for revenue-generating activities — selling, coaching, and strategic planning.

Activity	Current State	Future State	Annual Savings
Board report preparation	8–10 hrs/month manual work	15–30 min dashboard pull	\$14,400 – \$18,000
Pipeline segmentation	2–3 hrs/week manual calculation	Real-time dashboard with quick filters	\$15,000 – \$22,500
Manual quote creation	30–60 min per quote, error-prone	10 min CPQ-generated quote with e-sign	\$12,600 – \$30,000
Commission validation	Spreadsheet reconciliation	CRM-based validation workflow	\$3,600 – \$7,200

📌 These are **conservative estimates** based on current reported time spend. Actual savings may be significantly higher as the team scales.

RETURN ON INVESTMENT

The ROI: Investment vs. Return

This engagement pays for itself within 5–7 months through quantifiable savings alone — before accounting for pipeline visibility, faster sales cycles, or expansion revenue.

\$46,950

Total Investment

Fixed fee across 313 median hours at \$150/hr for the full two-phase CRM overhaul.

\$56K+

Year 1 Return

Conservative Year 1 return of \$56,400–\$106,500 from time savings and tool cost reduction alone.

5–7mo

Payback Period

Using only quantifiable, conservative estimates — before any revenue uplift is counted.

127%

Max Year 1 ROI

Year 1 net ROI range of 20%–127%, excluding revenue uplift from improved pipeline visibility and expansion revenue.

Tool Cost Reduction — \$10,800 – \$28,800/year

STRIVE is paying for Enterprise capabilities it isn't using — and evaluating external tools that HubSpot already includes.

Tool	Current/Planned Cost	Replaced By	Annual Savings
Apollo (under evaluation)	\$3,600 – \$12,000/year	HubSpot Breeze AI enrichment (included in Enterprise)	\$3,600 – \$12,000
External contract tool (PandaDoc, etc.)	\$6,000 – \$12,000/year	HubSpot CPQ (included in Enterprise)	\$6,000 – \$12,000
Unused HubSpot seats (5–8 service seats)	\$1,200 – \$4,800/year	Seat/license audit and consolidation	\$1,200 – \$4,800

- 📌 These savings are recurring and compound every year the tools remain eliminated. The longer STRIVE waits, the more it costs.

Pipeline Visibility & Expansion Revenue

\$150K+ in Pipeline Visibility

If 20% of active pipeline is uncaptured today, and the average deal is \$30K, capturing just 5 additional deals = \$150K+ in pipeline the board can see and track.

\$150K – \$750K Expansion Revenue

250 microsite clients from the Howden pack deal have no path to app upsell in the CRM today. Each converted client represents \$6K–\$30K in incremental revenue. If 10% convert: \$150K–\$750K.

Board Confidence

PE investors see operational maturity. Clean data and automated reporting signals the company is ready to scale. Board meetings shift from “explain the numbers” to “here are the numbers — let’s talk strategy.”

AI Readiness

Clean, classified, enriched CRM data is the prerequisite for AI-powered operations. This engagement builds the data foundation for Jodi’s AI knowledge assistant vision and every future AI initiative.
