



PROPOSAL

HUBSPOT CRM IMPLEMENTATION

Arkview Capital — HubSpot CRM Proposal

A tailored HubSpot Sales Hub Professional implementation to centralize deal management, streamline workflows, and replace fragmented tracking across your team.



A Note on This Proposal

Proposals are inherently a starting point — not a final blueprint. This document reflects our understanding of your challenges, a proposed solution, and the resources required to execute successfully.

We recognize that you live with these challenges daily, and there may be details we have yet to uncover. Our goal is to use this as a **conversation starter** — to refine, align, and ensure we are solving the right problems in the right order.

- ❏ If any aspect of the scope, solution, or pricing feels misaligned, let's use that as a basis for further discussion.

CHAPTER 1

Executive Summary

Arkview Capital is a **minority-certified private equity firm** headquartered in Stamford, CT, founded in 2020 by partners from the Ziff family office. With 7–8 professionals, Arkview invests in lower middle-market businesses across essential services, transportation, and financial services — including NEOTech and Icon Parking.

Single-Phase Rollout

6–8 weeks delivering both pipelines, contact management, Outlook integration, reporting, and training in one coordinated push.

Two Deal Pipelines

M&A and Real Estate pipelines with customized stages, required fields, and partner review tracking.

Why Professional?

Workflow automation, multiple pipelines, required fields per stage, and custom reporting all require Professional-tier capabilities.

Objectives

01

Centralize Contact Data

Replace fragmented tracking across email, LinkedIn exports, and individual records with a single HubSpot CRM.

03

Automate Workflows

Deal stage progression, NDA status tracking, partner review notifications, and task creation to reduce manual coordination.

05

Deliver Reporting Dashboards

Pipeline health, conversion rates, and deal velocity visibility across both M&A and Real Estate.

02

Configure Deal Pipelines

Two distinct pipelines — M&A and Real Estate — with customized stages, required fields, and partner review tracking.

04

Integrate Outlook

Seamless Microsoft 365 email logging, calendar sync, and contact capture across the deal team and EA.

06

Migrate & Train

Clean contact import via template, plus role-appropriate training for Frank (admin), deal team, EA, and optionally Jess.

Why HubSpot Sales Hub Professional?

Sales Hub Professional is recommended over Starter because Arkview’s core requirements demand Professional-tier capabilities.



Workflow Automation

Deal stage progression, NDA tracking, partner review notifications, and task creation all require Professional. Starter does not support custom workflows.



Required Fields per Stage

Enforcing data entry at stage gates (e.g., requiring NDA status before advancing) is a Professional feature.

Future-Proofing

When investor communications, LP management, or marketing tools are added later, Professional provides the foundation without re-platforming.



Multiple Pipelines

Two distinct pipelines (M&A and Real Estate) with different stage definitions require Professional. Starter limits pipeline customization.



Custom Reporting

Conversion rate and pipeline health reports across two pipelines require Professional’s custom report builder.

Estimated Licensing

~\$90–100/user/month for Professional

5 paid seats = ~\$450–500/month

View-only seats for Jess and Brian at no additional cost.

Workstream 1: CRM Architecture & Setup

Arkview needs a professionally configured HubSpot environment supporting their small fund team with appropriate access controls, FINRA-compliant settings, and clear role distinctions.

1

Portal Configuration

Sales Hub Professional with Arkview branding, company settings, and naming conventions.

2

User Roles & Permissions

5 paid seats (Frank, Pavel, Vijay, Philip, EA) + view-only for Jess and Brian. Teams aligned to M&A, Real Estate, and Operations.

3

Security & Compliance

Data access controls for a PE firm. FINRA-compliant tracking settings reviewed (email tracking pixels, data residency) — compliance counsel sign-off is client responsibility.



Workstream 2: Contact & Company Management

Track relationships across deal sourcing contacts, vendors, LPs, lenders, and portfolio companies in a structured system reflecting the complexity of a PE fund's relationship network.

Configuration

- Up to 25 **custom properties** tailored to PE fund workflows
- Lifecycle stages: Unknown → Known Opportunity → Active Deal → Portfolio Company → Sold
- Parent-child company structures for PE firm-to-portfolio relationships
- Contact categories: deal sourcing, vendors, LPs, lenders


Data Quality

- Association labels and segmentation lists for key contact categories
- Deduplication strategy with automated detection rules
- Ongoing data hygiene standards established from day one

Workstream 3: M&A Pipeline

A structured M&A deal pipeline to track investment opportunities from sourcing through close, with stage gates enforcing data discipline and partner review tracking.

Deal Stages

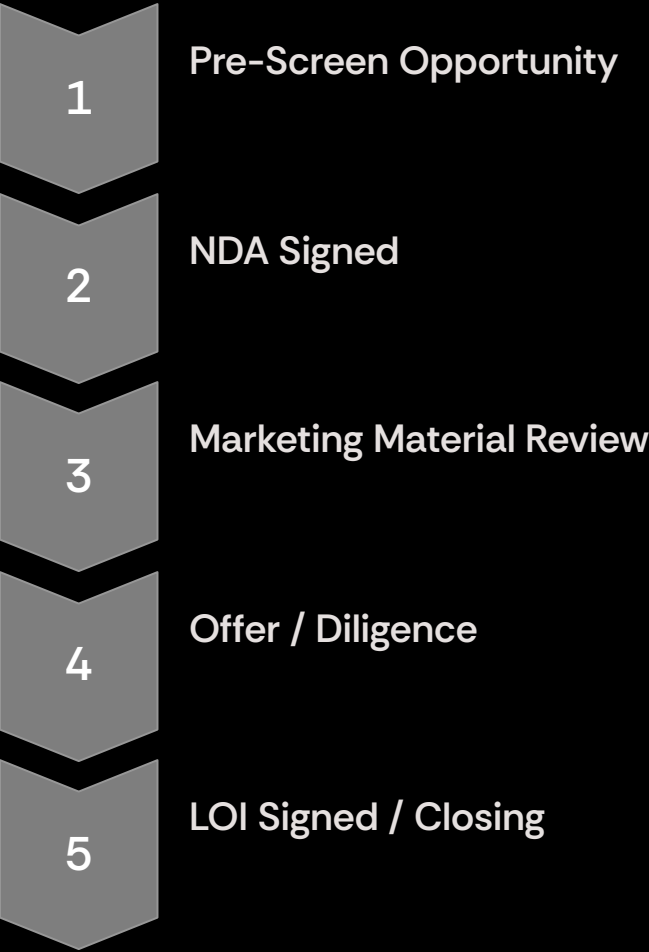

Key Configuration

Required Fields per Stage Enforce data completeness at each gate (e.g., NDA status before advancing).
Partner Review Tracking Checkbox properties for each partner’s review status ensure alignment before deals advance.
Closed-Won Automation Triggers lifecycle stage update to Portfolio Company automatically.

Workstream 4: Real Estate Pipeline

Vijay and Philip's real estate team needs a **separate pipeline** for parking garage and real estate acquisition deals with customized stages and tracking fields specific to the real estate investment lifecycle.

Separate Pipeline

Customized stages TBD pending discovery call with Vijay and Philip.

RE-Specific Properties

Deal properties, required fields, and stage progression rules tailored to real estate acquisitions.

Team Views & Filters

Dedicated deal views for real estate team management and reporting.

- 📌 **Contingent:** Stages TBD pending discovery with Vijay and Philip. If discovery cannot be scheduled within 2 weeks of engagement start, a placeholder pipeline with generic stages will be built and refined later.



Workstream 5: Automations & Workflows

Reduce manual coordination and ensure consistent deal progression by automating stage notifications, partner review reminders, NDA tracking, and task creation.

1 Deal Stage Notifications

Automated alerts when deals progress through pipeline stages.

2 Partner Review Reminders

Notification and reminder workflows to keep partner reviews on track.

3 NDA Status Tracking

Checkbox-based automation (no e-signature integration).

4 Lifecycle Automation

Deal-to-Portfolio Company lifecycle update on Closed-Won.

5 Task Creation

Automatic tasks for new deal stages and follow-up actions.

6 Lead Routing

Basic routing rules to assign incoming opportunities.

Requires Sales Hub Professional. Up to 8 automated workflows included. All workflows documented for ongoing admin management by Frank.


Workstream 6: Outlook Integration

Seamless integration between Microsoft 365 / Outlook and HubSpot so emails, meetings, and calendar activity are automatically captured without disrupting established habits.



Outlook Add-In

HubSpot Sales Extension configured for 5 users with connected inbox setup per user.



Calendar Sync

Automatic meeting capture, logging, and meeting link functionality configured.



FINRA Compliance

Email tracking pixels disabled by default until cleared with compliance. Domain exclusions prevent logging internal communications.

Outlook integration stability validated during Week 1 with fallback plan (BCC forwarding) if needed.

Workstream 7: Reporting & Dashboards

Visibility into pipeline health, deal velocity, and conversion rates across both pipelines through purpose-built dashboards supporting Frank's management of deal flow.

1

M&A Dashboard

Stage conversion and velocity metrics for the investment pipeline.

2

Real Estate Dashboard

Parallel reporting for parking garage and RE acquisition deals.

3

Activity Reports

Deal activity and contact engagement tracking across teams.

By the Numbers

2–3 dashboards with up to 8 custom reports


Uses HubSpot Professional custom report builder.

Breeze AI note search configured (best-effort — new feature with limited guarantees).

Historical data available only from go-live date forward.

Workstream 8: Data Migration

Consolidate contacts currently scattered across LinkedIn exports, email records, and individual knowledge into a single, clean CRM database.

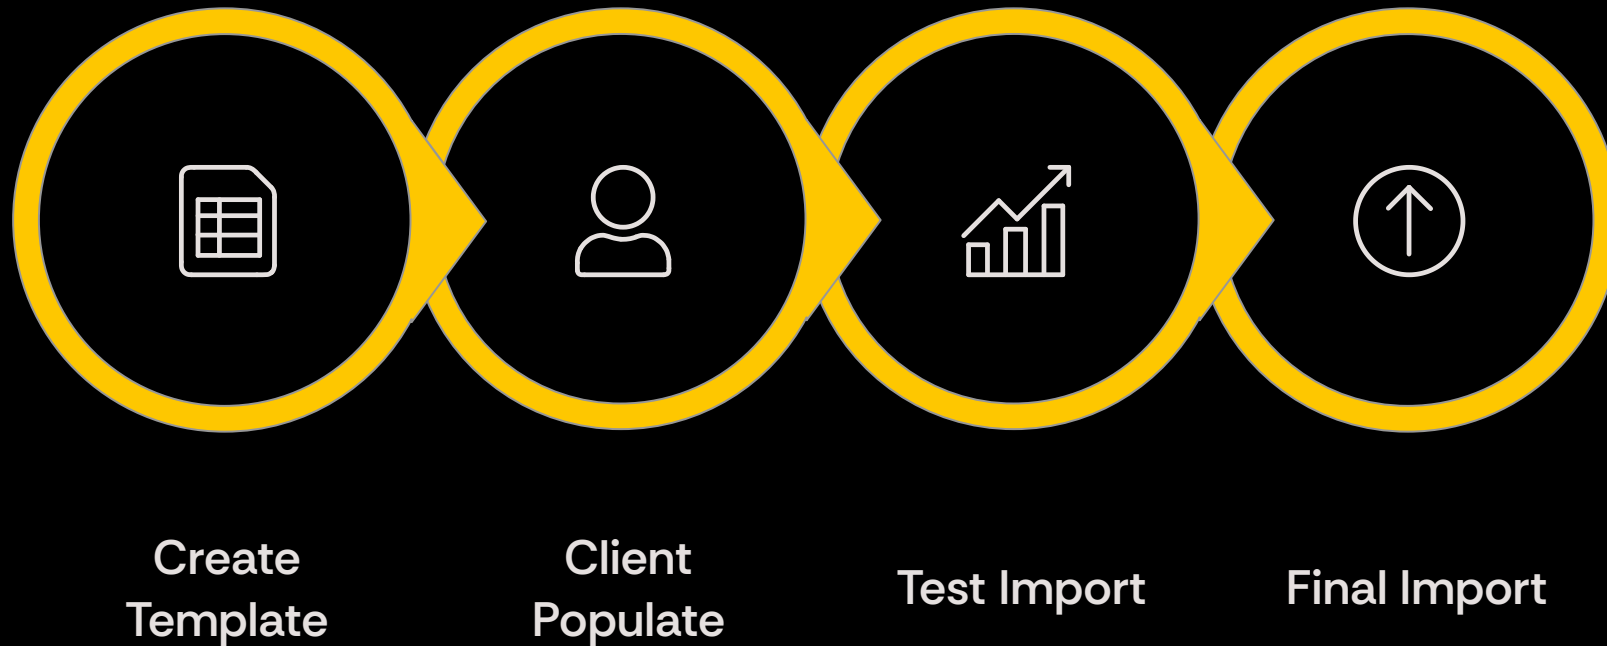

Under **1,000 contacts** for initial import. Does not include historical activity or deal data migration. If volume exceeds 1,000 contacts or requires multi-source merging, a change order applies.



Workstreams 9–11: Training

Role-appropriate training ensures every team member is confident in their specific CRM workflows from day one.

Admin Training (Frank)

1–2 sessions. Portal settings, property management, pipeline configuration, workflow editing, reporting, user management, and ongoing maintenance. Frank becomes a self-sufficient HubSpot administrator.

End User Training

1–2 sessions. Daily CRM usage, Outlook add-in, deal updates, contact management, and mobile app for Pavel, Vijay, Philip, and EA. May split M&A and Real Estate teams.


Operations (Optional)

30-minute walkthrough for Jess covering basic CRM navigation and email tool orientation. Only needed if Jess will use email or marketing features.

All sessions delivered virtually via screen share.

Workstream 12: UAT, Go-Live & Documentation

A controlled go-live process with testing, documentation, and post-launch support ensures smooth transition and sustained adoption.

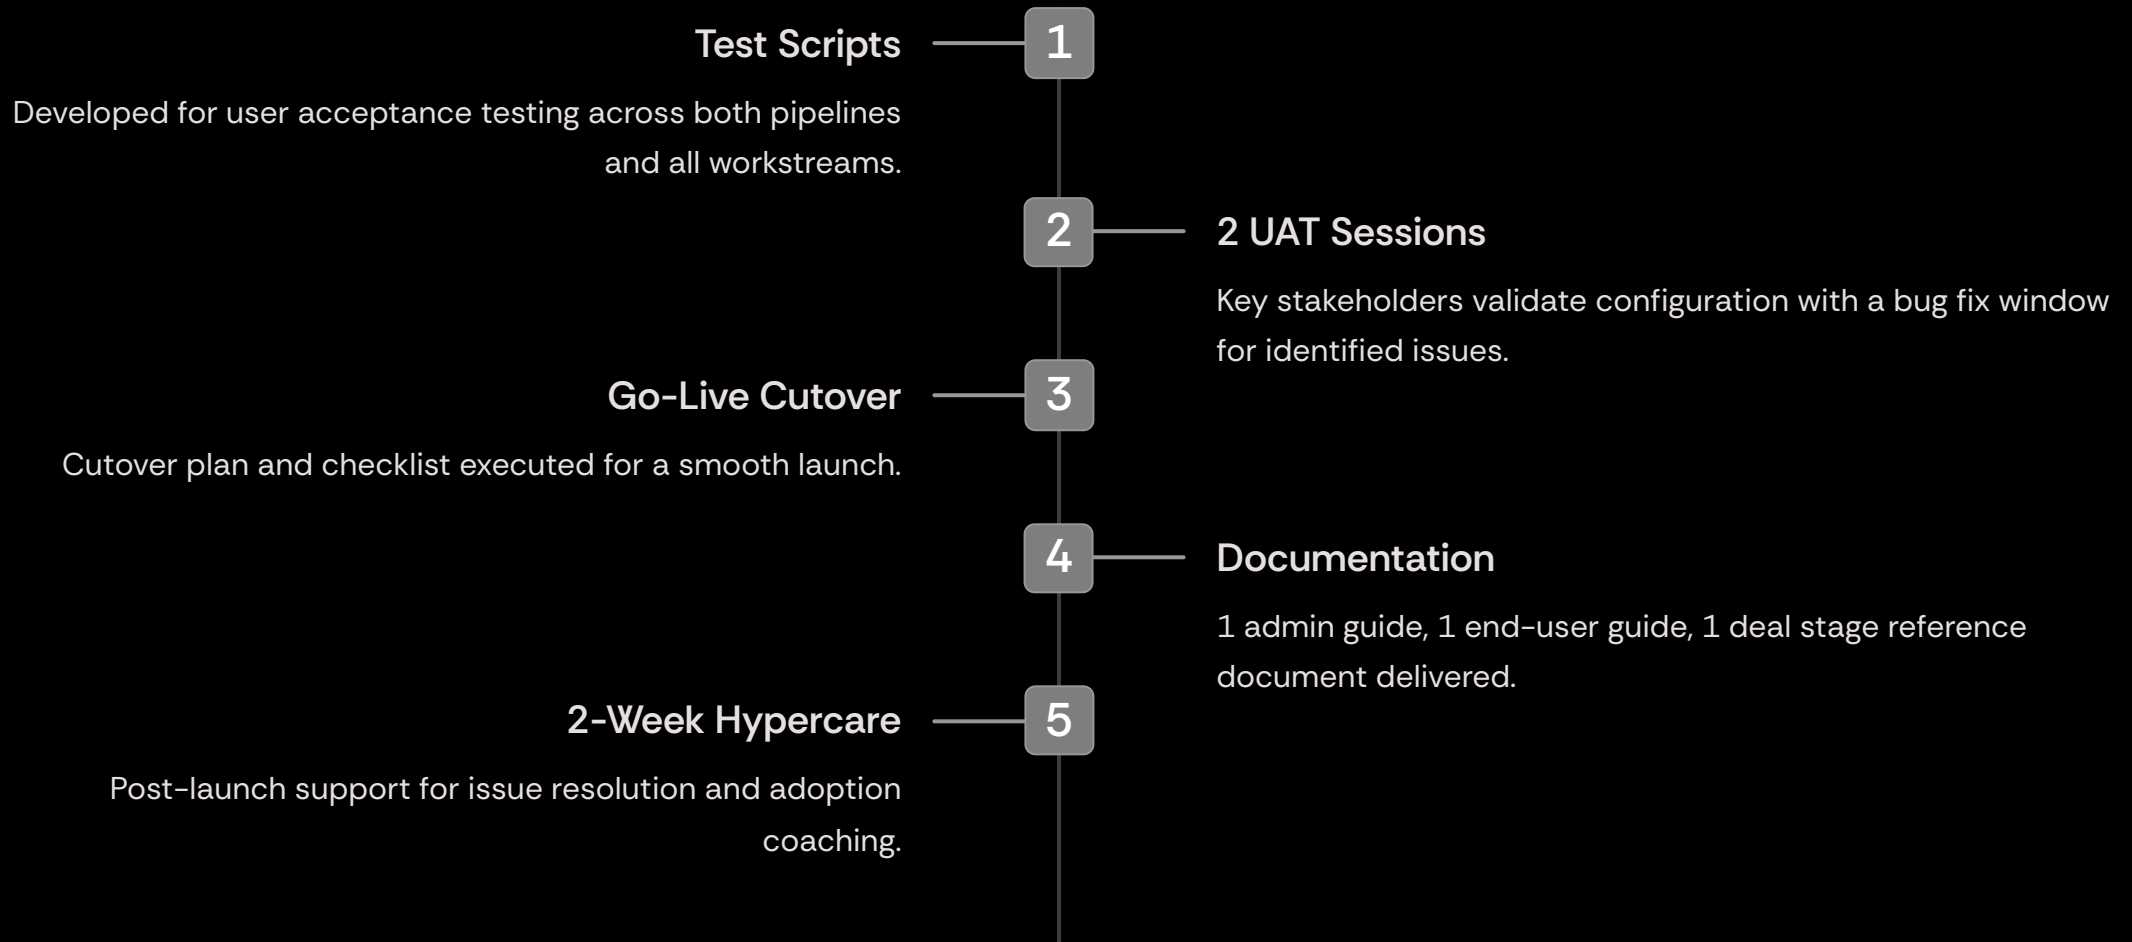

CHAPTER 5

Deliverables & Timeline

Single-phase rollout over 6–8 weeks delivering the complete CRM foundation.

Weeks 1–2	CRM architecture & setup, contact/company management, Outlook integration, data migration template
Weeks 3–4	M&A pipeline build, Real Estate pipeline build, automations & workflows
Weeks 5–6	Reporting & dashboards, training sessions (admin + end user)
Weeks 6–8	UAT testing, documentation delivery, go-live cutover, 2-week hypercare support

Engagement Model & Pricing

\$22,750

Fixed Fee

Total project delivery cost

6–8

Weeks

Project timeline

5%

Tech & Admin Fee

Applied to each invoice

Payment Terms

- 4 equal installments of \$5687.50, billed semi-monthly beginning on project start date.
- Net-15 terms on all invoices

HubSpot Licensing (Separate)

~\$450–500/month for 5 Sales Hub Starter seats.

Procured directly by Arkview Capital from HubSpot. View-only seats for Jess and Brian at no additional cost.

Project Governance

Sayer Responsibilities

- Lead configuration, QA, and implementation across all workstreams
- Weekly 30-minute check-ins and milestone reviews
- Documentation, training, and go-live support
- Manage timeline and proactively communicate risks or blockers

Arkview Responsibilities

- Populate contact import template with accurate data by Week 2
- Provide RE pipeline stage definitions (Vijay/Philip) before build begins
- Procure HubSpot Professional licenses before implementation
- Designate Frank as primary POC for decisions and approvals
- Ensure team availability for training sessions
- Review configuration with FINRA compliance counsel before go-live
- Provide M365 admin access for Outlook integration
- Complete UAT testing within agreed timeline

Assumptions & Constraints

In Scope

- HubSpot Sales Hub Professional tier
- 5 paid seats + view-only for Jess and Brian
- Microsoft 365 / Outlook integration
- Up to 25 custom properties
- 2 pipelines: M&A (5 stages) and RE (TBD)
- Up to 8 automated workflows
- 2–3 dashboards, up to 8 custom reports
- Under 1,000 contacts for initial import
- NDA tracking is manual checkbox
- All work conducted remotely

Out of Scope

- Marketing Hub / marketing automation
- Investor communications & LP management
- DocuSign or e-signature integration
- Call recording / meeting transcription (FINRA)
- PitchBook or data enrichment tools
- Detailed diligence tracking (remains in Excel)
- Custom API development or middleware
- Service Hub or Operations Hub features
- LinkedIn Sales Navigator integration
- Managed services beyond 2-week hypercare
- FINRA compliance audit

Any scope changes require formal approval and may impact cost or timing.

CHAPTER 9

Future Capabilities

These were discussed during discovery and are explicitly deferred. They represent natural next steps once the CRM foundation is established.



Investor Communications & LP Management

Requires discovery with Jess and Brian. Could include LP contact tracking, fundraising pipeline, investor reporting dashboards, and communication logging.



Marketing Tools

LinkedIn posting, email campaigns, and basic marketing automation through HubSpot Marketing Hub.



E-Signature Integration

DocuSign or similar tool to automate NDA execution and deal stage progression based on signature status.



Advanced Reporting & AI

Breeze AI enhancements, advanced deal scoring, and weighted pipeline analysis.



CHAPTER 10

Approval & Next Steps

Please confirm alignment on scope and structure so we can move forward with scheduling a formal kickoff and assigning your Sayer team.

1

Written Approval

Provide written approval of this proposal via email.

2

RE Discovery Call

Schedule Real Estate pipeline discovery with Vijay and Philip (required before kickoff).

3

Project Kickoff

Schedule within 1–2 weeks of written approval.

- Upon written approval, Sayer will issue a Master Services Agreement (MSA) via DocuSign, with this Scope of Work included. Once the MSA is executed, Sayer will finalize the implementation plan and begin onboarding.
