

HUBSPOT CRM PROPOSAL

The Milestone Group — HubSpot CRM Implementation

A phased approach to centralizing relationship management, capturing deal activity, and replacing fragmented tracking — designed for adoption across every office and every team member.



Executive Summary

The Milestone Group is a national private equity real estate investment management firm with industry-leading returns since inception in 2003 and over \$7 billion in real estate investments. With approximately 45 team members across offices in Dallas, Boca Raton, Atlanta, and a fourth location, Milestone manages apartment acquisitions across major U.S. metropolitan markets on behalf of leading institutional investors, pension funds, and sovereign wealth funds.

Phase 1

Weeks 1–4: Contact management & activity capture

Phase 2

Weeks 5–6: Deal pipeline configuration


Phase 3

Weeks 7–8+: Integrations & advanced features

📌 This implementation establishes a CRM foundation that Milestone can expand over time as additional workflows and integrations are identified. A phased approach is strongly recommended based on Milestone's stated preference for starting simple and expanding. Team members range from 25 to 65 years old with varying technology comfort levels. The previous DealCloud abandonment after two months underscores the adoption risk of an all-at-once approach.

Project Objectives

This engagement is designed to solve Milestone’s core challenges — fragmented data, inconsistent tracking, and limited executive visibility — through a unified CRM foundation.

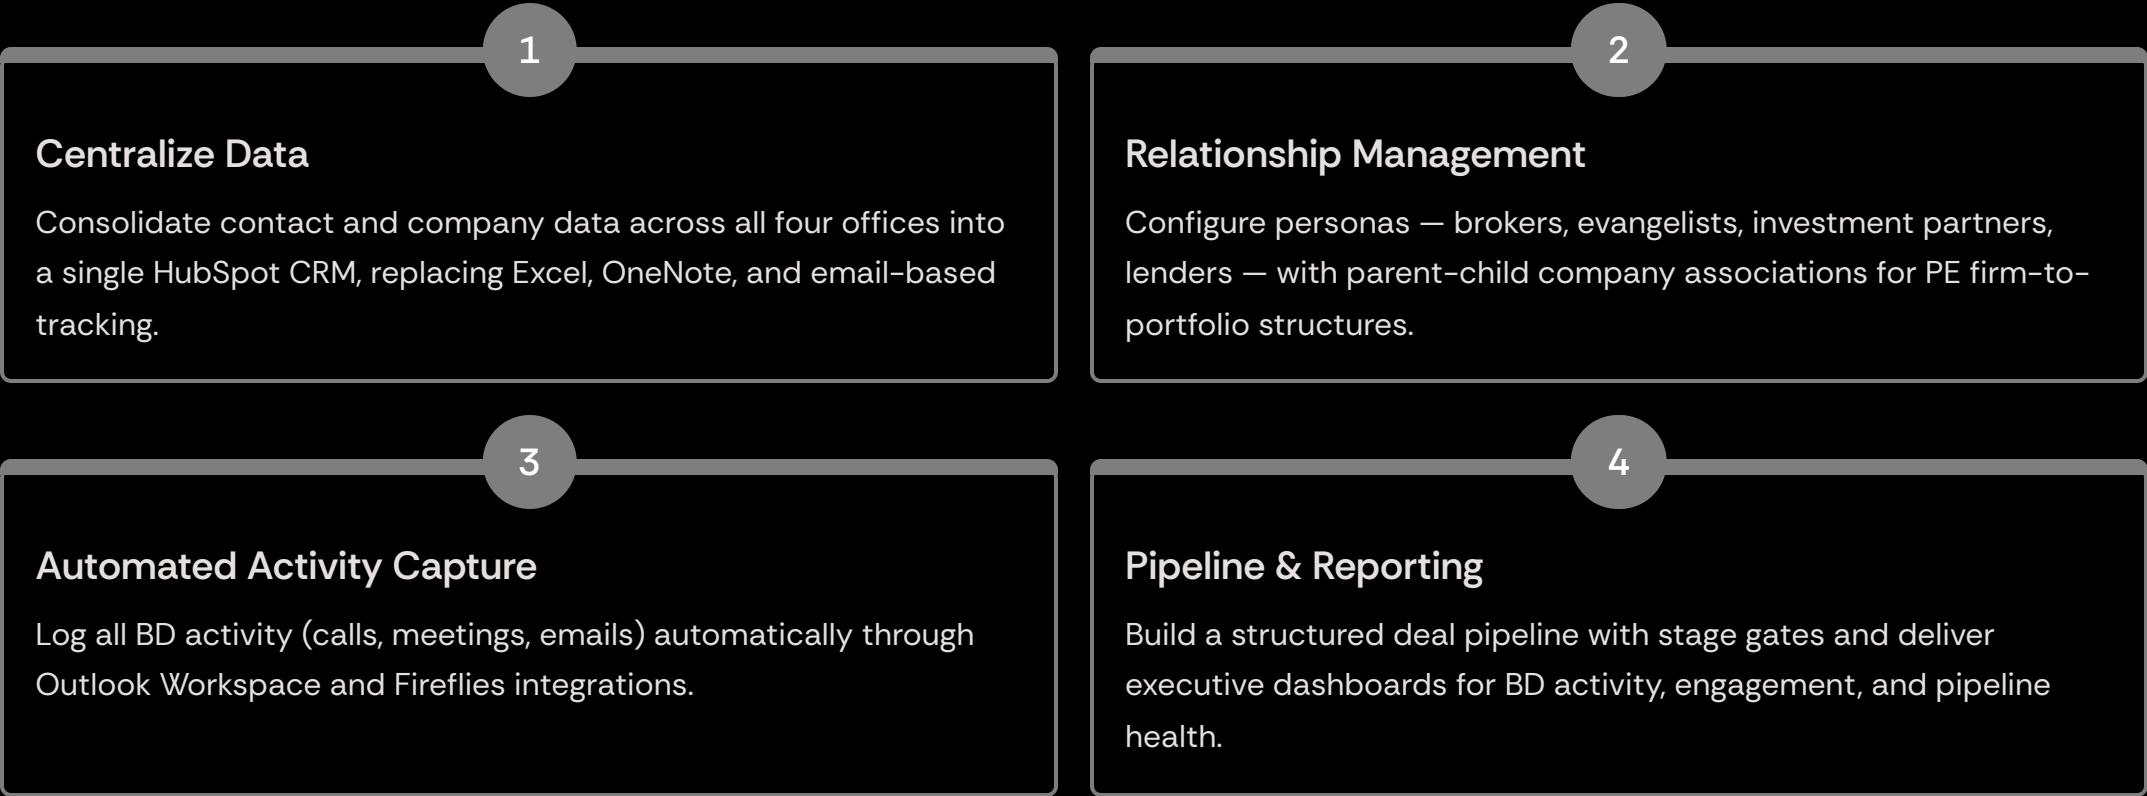

2K–5K

Contacts to Migrate

From multiple overlapping sources

4

Offices

Nationwide team coverage

10

CRM Users

Licensed seats across locations

CRM Architecture, Contacts & Data Migration

Phase 1 (Weeks 1–4) establishes the CRM foundation — delivering immediate value with minimal behavior change so the team builds confidence before adding complexity.

Workstream 1: CRM Architecture & Setup

- HubSpot portal with Milestone branding
- User roles & permissions for up to 10 users across 4 offices
- Team structure aligned to office locations
- Naming conventions & security settings for PE firm standards

Workstream 2: Contact & Company Management

- Up to 30 custom contact/company properties
- Lifecycle stages for prospect-to-active progression
- Parent-child associations for PE firm-to-portfolio structures
- Persona categories: broker, evangelist, investment partner, lender
- Deduplication rules for ongoing data quality

Workstream 3: Data Migration

1

Audit

Assess data across all sources for volume, quality, and completeness

2

Map & Cleanse

Field mapping, standardization, and deduplication in staging

3

Test Load

Validate mapping, formatting, and association accuracy

4

Final Import


Production import with post-migration validation and cleanup

Email, Communications & Automations



Workstream 4: Email & Communication Setup

Configure Outlook integration for email and calendar per user. Set up connected inboxes, email tracking with opt-in preferences, domain exclusions for internal communications, and calendar sync for automatic meeting capture.



Workstream 5: Automations & Workflows

Build up to 8 automated workflows covering activity capture rules, task reminder triggers for follow-up actions, workflows based on meeting outcomes, and automatic contact creation rules with email domain exclusions. All workflows documented for ongoing admin management.

Pipeline, Integrations & Reporting

With the foundation established, Phases 2 and 3 layer on deal tracking, third-party integrations, and executive-level reporting dashboards.

1

Workstream 6: Pipeline & Deal Management

Phase 2 (Weeks 5–6) — Build custom deal pipeline with stages aligned to Milestone’s investment process. 1 primary pipeline with 4–6 stages, required fields per stage for data discipline, and qualification criteria with stage gate enforcement.

2

Workstream 7: Fireflies Integration

Phase 3 (Weeks 7–8+) — Configure native Fireflies-to-HubSpot integration for automated meeting transcription logging. Includes transcript mapping, contact matching logic, and validation with sample meetings before go-live.

3

Workstream 8: Outlook Workspace Sync

Phase 3 (Weeks 7–8+) — Calendar sync automation, contact sync rules between Outlook Contacts and HubSpot, sync frequency and conflict resolution rules, with per-user sync validation.

4

Workstream 9: Reporting & Dashboards

2–3 dashboards covering BD activity (calls, meetings, emails by team member), contact engagement with lifecycle tracking, and deal pipeline with stage conversion and velocity metrics. Up to **10 custom reports** with scheduled email delivery.

Training, UAT & Launch

A controlled go-live process ensures smooth transition and sustained adoption across all offices and age groups.


Workstream 10: Training & Enablement

- **1–2 admin training sessions** for designated power users covering settings, properties, workflows, and reporting
- **2–3 end-user sessions** tailored to varying technical comfort levels (ages 25–65)
- Daily CRM usage, mobile app setup, activity logging, and task management
- Hands-on guidance for each office's specific workflow patterns
- Sessions recorded for future onboarding of new team members

Workstream 11: UAT & Go-Live

- Test scripts for user acceptance testing across all workstreams
- **2 UAT sessions** with key stakeholders
- Bug fix window for issues identified during testing
- Go-live cutover plan and checklist
- **3 documentation deliverables:** admin guide, end-user guide, mobile quick-start guide
- **2-week hypercare support** post-launch

Timeline & Pricing

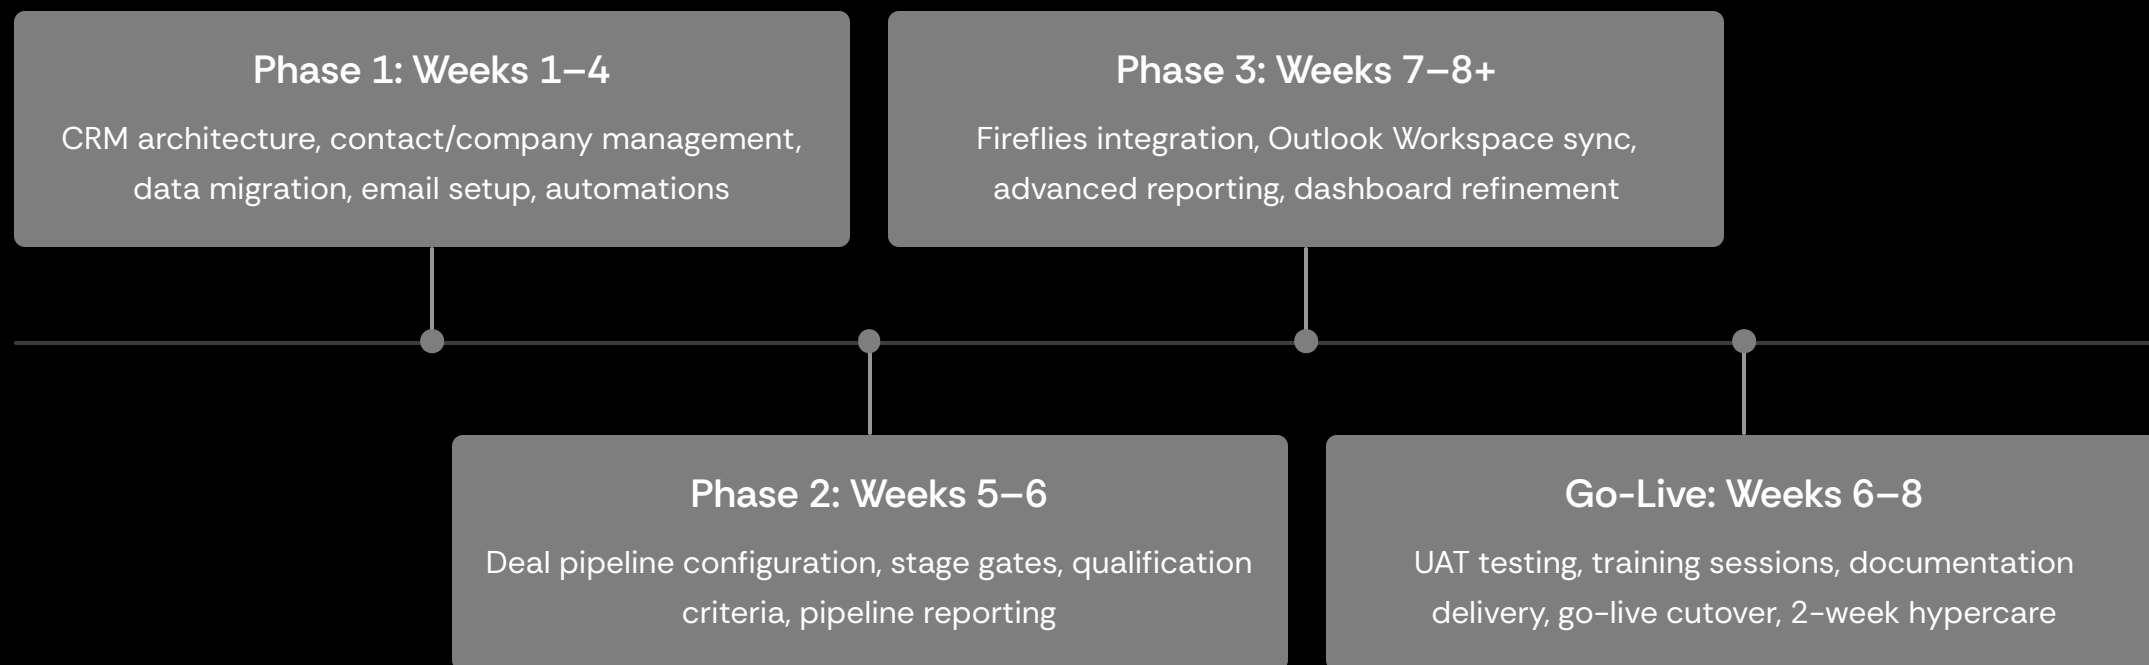

Investment

\$26,075

Fixed Fee

4 equal installments of \$6,518.75, billed semi-monthly beginning on project start date. Net-15 terms on all invoices.

A 5% Technology & Administrative fee is applied to each invoice to offset costs of our technology stack and internal systems.

Key Deliverables

- Configured HubSpot CRM with branding & team structure
- Contact/company management with persona tagging & parent-child associations
- Data migration of 2,000–5,000 contacts
- Outlook Workspace & Fireflies integrations
- 8 automated workflows
- Deal pipeline with stage gates
- 2–3 reporting dashboards with up to 10 custom reports
- Training sessions & 3 documentation guides

Project Governance & Responsibilities

Sayer Responsibilities

- Lead configuration, QA, and implementation across all workstreams
- Conduct weekly check-ins and milestone reviews
- Provide documentation, training, and go-live support
- Manage project timeline and proactively communicate risks or blockers

Milestone Group Responsibilities

- Provide complete contact exports by week 2
- Designate 1 primary point of contact for decisions
- Ensure stakeholder availability for discovery, UAT, and training
- Procure HubSpot licenses & confirm Fireflies subscription with API access
- Provide Outlook Workspace admin access
- Champion CRM adoption internally — leadership must set usage expectations

 **Out of Scope:** Salesforce/Zoho, ERP/accounting integration, Asana integration, advanced deal scoring, custom API development, marketing automation, DocuSign integration, Service/Operations Hub features, and ongoing managed services beyond 2-week hypercare.



 LET'S GET STARTED

Approval & Next Steps

This proposal reflects our understanding of your challenges and a proposed solution. If any aspect of scope, phasing, or pricing feels misaligned, let's use that as a basis for further discussion.

1 Provide Written Approval

Confirm alignment on scope and structure via email

2 Schedule Kickoff

Project kickoff within 1–2 weeks of written approval

3 Execute MSA

Sayer will issue a Master Services Agreement via DocuSign with this Scope of Work included


4 Begin Onboarding

Once the MSA is executed, Sayer will finalize the implementation plan and begin onboarding

We recognize that you, as the client, live with these challenges daily. Our goal is to use this as a conversation starter — to refine, align, and ensure we are solving the right problems in the right order.

Future Integration: HubSpot → Asana Integration

Connect deal tracking in HubSpot with project execution in Asana.



Benefits

- Eliminates manual handoffs between teams
- Keeps BD and operations aligned
- Maintains deal visibility through execution

Potential Timing

Implemented after CRM adoption, once workflows are established. The integration is native to HubSpot and can be enabled quickly, but configuration and workflow design (if necessary) would occur as a future phase outside the current engagement.
