


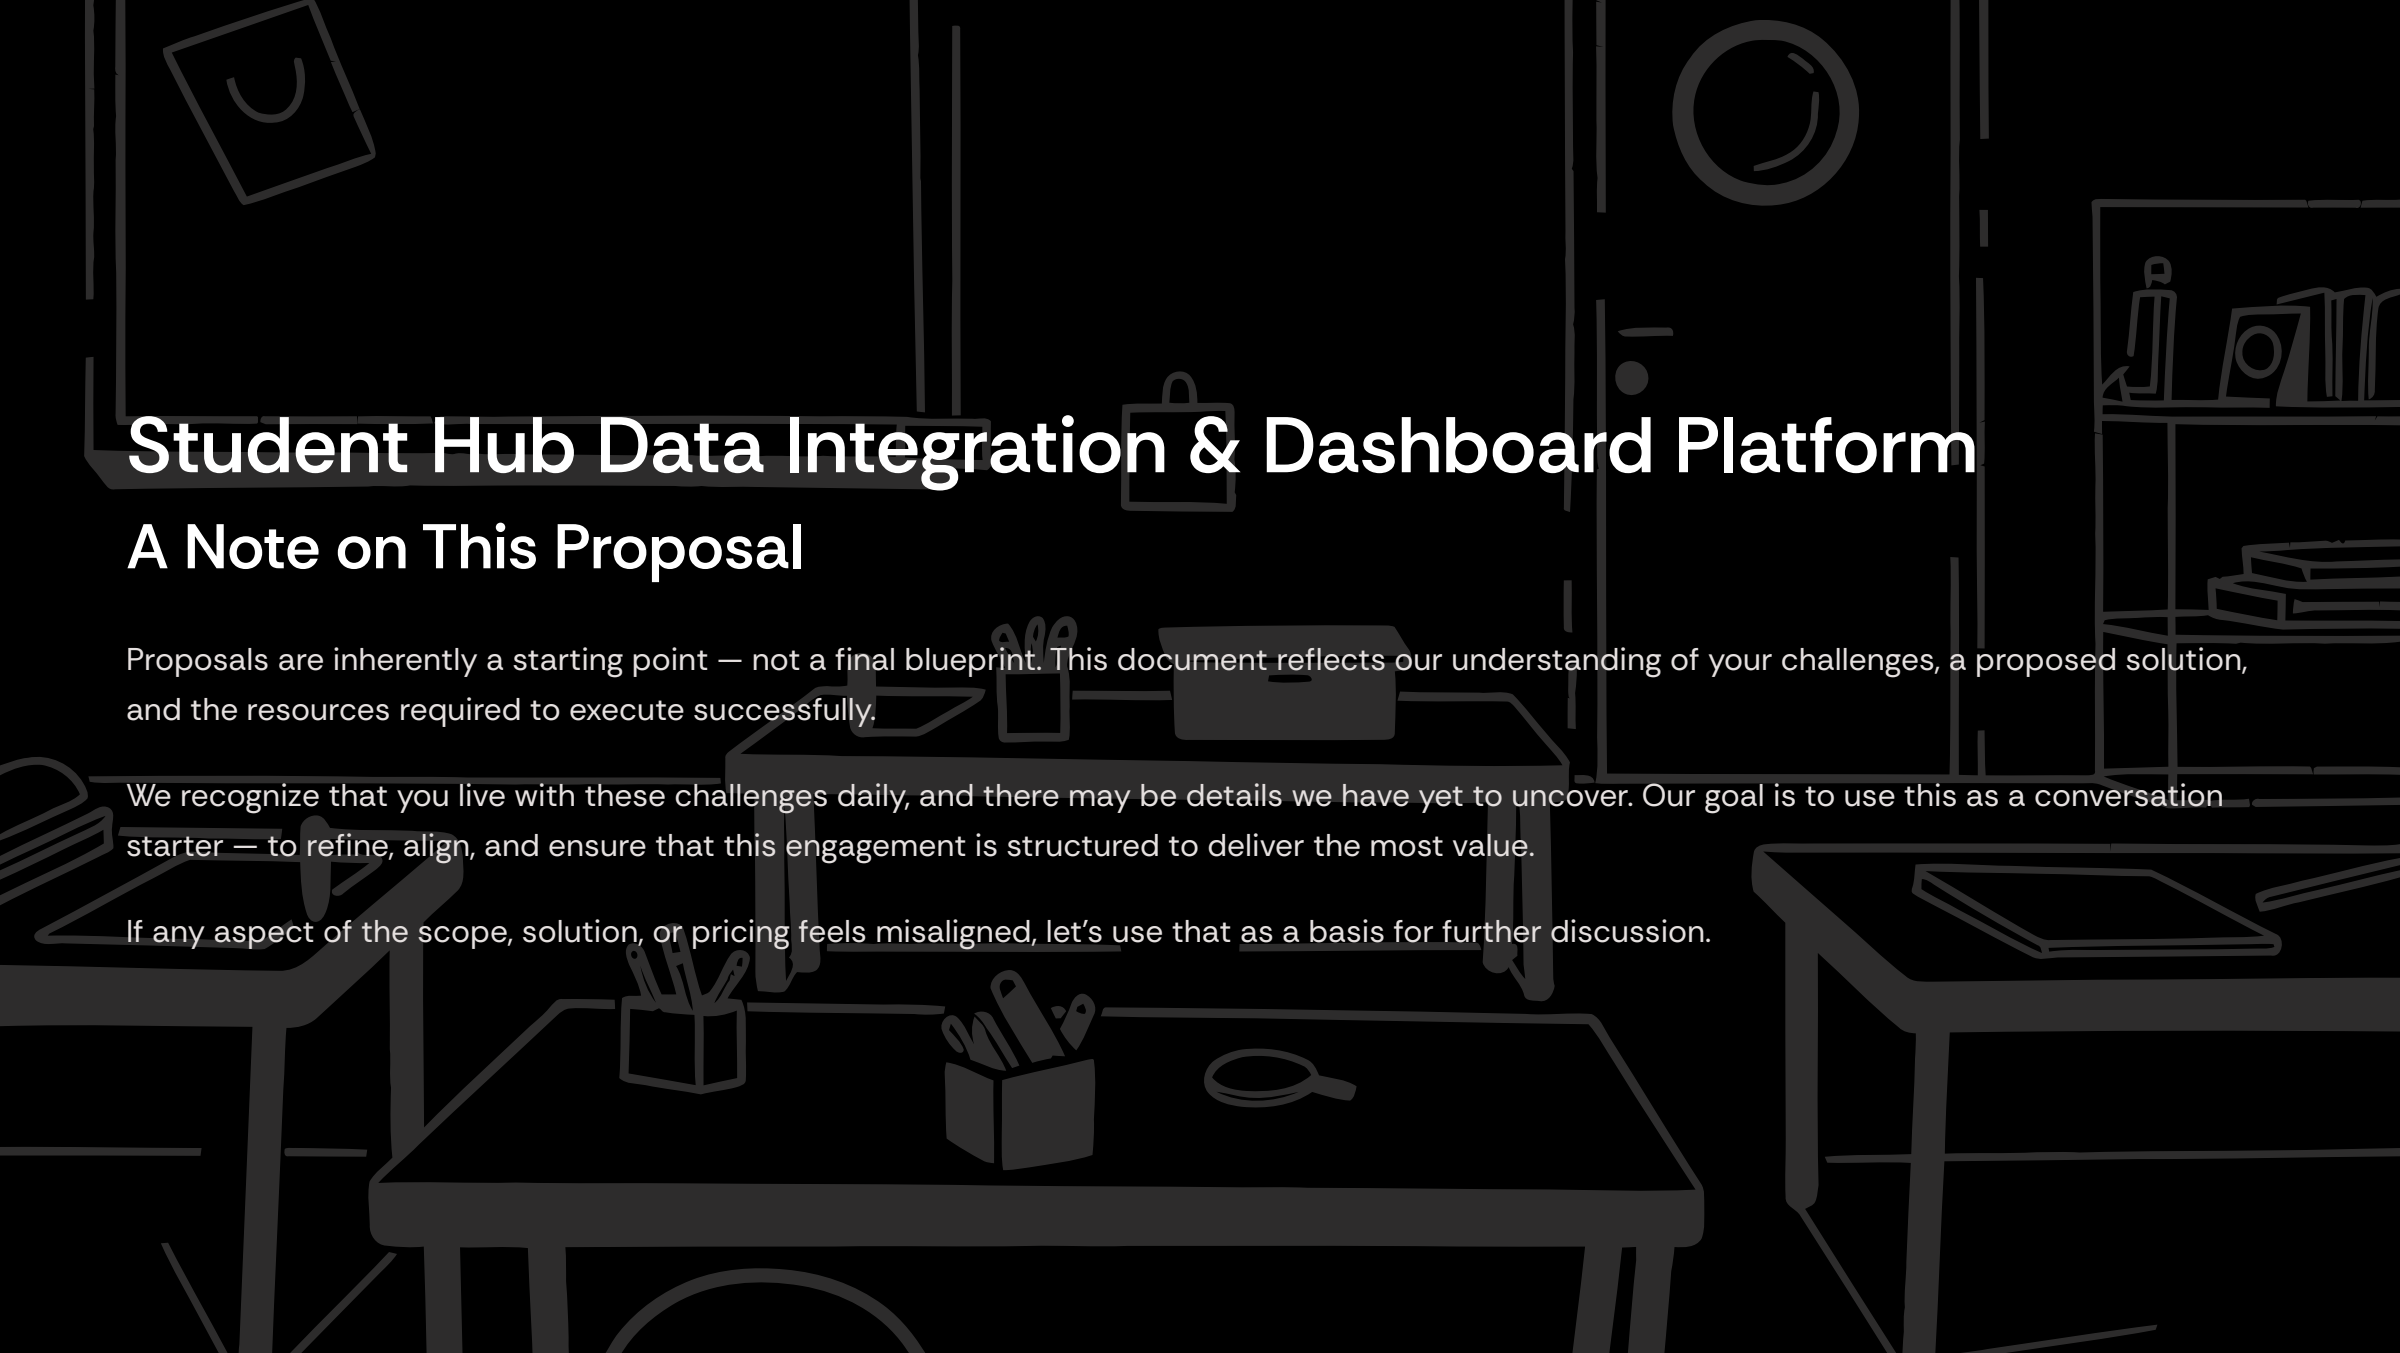

Student Hub Data Integration & Dashboard Platform

A Note on This Proposal

Proposals are inherently a starting point — not a final blueprint. This document reflects our understanding of your challenges, a proposed solution, and the resources required to execute successfully.

We recognize that you live with these challenges daily, and there may be details we have yet to uncover. Our goal is to use this as a conversation starter — to refine, align, and ensure that this engagement is structured to deliver the most value.

If any aspect of the scope, solution, or pricing feels misaligned, let's use that as a basis for further discussion.

Executive Summary

The Challenge

Crux Capital's franchise system is operating with fragmented visibility. Financial data lives in QuickBooks Online across franchises, operational and enrollment data sits in Student Hub, and leadership lacks a unified view to identify declining locations, benchmark performance, or calculate system-wide royalties with confidence.

Sayer's Solution

A focused 12-week data integration and dashboard engagement designed to unify Student Hub and QuickBooks Online data into a functional reporting platform that enables:

- System-wide revenue and royalty visibility for corporate leadership
- Franchisee-level operational scorecards for benchmarking and accountability
- Financial deep-dive reporting for performance analysis

This engagement is intentionally structured to create a working foundation — not a multi-year transformation program. We build what works, validate with real users, and create a platform that can scale as your system grows.

Our Understanding of Your Needs

The Current Reality



Fragmented data across systems

- Student Hub holds enrollment, staffing, and operational data
- QuickBooks Online contains financial data across ~70 franchises
- No unified view for leadership or franchisees



Limited visibility into system health

- Difficult to identify declining locations quickly
- No standardized benchmarking across franchises
- Royalty calculations are manual and time-consuming



Growing system complexity

- Plans to expand from 70 to potentially 500 franchises
- Need for scalable infrastructure that grows with the business
- Risk of building solutions that don't scale

What Success Looks Like



For Franchise Owners

- Operational scorecard showing their performance vs. budget and peers
- Clear visibility into key metrics: revenue, enrollment, staff ratios
- Rankings and benchmarks for self-assessment



For Finance & Operations

- Detailed P&L reporting with trend analysis
- Marketing spend visibility
- Reliable month-over-month and year-over-year comparisons



For Crux Capital

- Single dashboard showing system-wide sales, royalty pool, and new enrollments
- Immediate visibility into declining locations and compliance issues
- Regional performance comparisons

Scope of Work

Data Sources & Integration

Included in Scope:

- Student Hub (enrollment, staff, operational data) via documented API
- QuickBooks Online (financial data) via documented API
- Automated daily or weekly refresh cadence as required

Assumptions:

- Both systems have well-documented APIs (per initial discussion)
- QBO deployment is consistent across franchises (field names, definitions, calculations)
- If QBO deployment varies significantly across franchises, additional discovery and mapping work may be required (potential +/-10% cost adjustment)

Infrastructure & Cloud Platform

Client Responsibility:

- Infrastructure procurement and ongoing costs (AWS, Azure, Snowflake, BigQuery, or similar)
- API access credentials for Student Hub and QuickBooks Online

Sayer's Role:

- Facilitate infrastructure selection and setup as part of engagement
- Design scalable data architecture appropriate for current and future needs
- Configure automated data pipelines and transformation layer

Optional Add-On:

- Non-standard offline data sources (structured files available online with defined sharing mechanism)
- Estimated impact: ~5% cost increase if required

Dashboard Development: Two Technology Approaches

We propose two alternative approaches for the reporting layer. Each has distinct trade-offs in upfront cost, ongoing expenses, and customization flexibility.

Option 1: Power BI Dashboard Platform

What You Get:

- Faster initial development timeline
- Familiar Microsoft ecosystem integration
- Standard dashboard interactions and drill-through
- Lower upfront development cost

Trade-offs:

- Higher ongoing licensing costs (~\$1,200/month for 70 franchises, scaling to ~\$4,500/month for 500 franchises)
- Less customization flexibility
- Standard Power BI look and feel

Best For:

- Organizations prioritizing speed to market
- Teams already using Microsoft tools
- Situations where standard dashboard functionality is sufficient

Option 2: Custom React-Based Application

What You Get:

- Fully customized interface and user experience
- Greater flexibility for future feature additions
- Significantly lower ongoing infrastructure costs (~\$600/month for 70 franchises, scaling to ~\$2,500/month for 500 franchises)
- Ownership of the codebase

Trade-offs:

- Higher upfront development cost
- Longer initial development timeline
- Requires technical resources for future modifications

Best For:

- Organizations planning to scale significantly
- Teams wanting control over long-term product roadmap
- Situations where custom workflows or integrations are anticipated

📌 **Sayer's Recommendation:** We will help you evaluate both options based on your growth timeline, budget constraints, and internal technical capabilities once we understand more about your long-term vision and organizational context.

Dashboard Coverage

The engagement includes three core reporting views:

1	The "HQ / Royalty" Dashboard Target Audience: Corporate Leadership (Kale, Drew, PE Investors) Key Metrics: - Total System Sales (system-wide revenue) - Total Royalty Pool (calculated from sales) - New Enrollments (system-wide) - Declining Locations: Campuses where revenue has dropped for 3+ consecutive months - Compliance Flags: Franchisees late on P&L submission or royalty payments - Regional Performance: Comparative profitability by region (e.g., Texas vs. Florida)
2	The "Franchisee Scorecard" (Operational Health) Target Audience: Individual Franchisee Owners Key Metrics: - Net Revenue: Actual vs. Budget - Enrolled Students: Current count and trends - Staff-to-Student Ratio - Rank/Benchmark: Performance vs. peer franchises
3	The "P&L Performance" Report (Financial Deep Dive) Target Audience: Franchisee Owners & Finance Team Key Metrics: - Revenue Breakdown: Tuition, Fees, Merchandise (mapped from QBO categories) - Marketing Spend Analysis - Trend Analysis: Month-over-Month (MoM) and Year-over-Year (YoY) growth charts



Note on Scope Boundaries: The three dashboards above represent the baseline scope. Additional reports, views, or custom analytics can be added but will require incremental effort and cost adjustment based on complexity.

Distribution of reports to stakeholders and franchises will be manual in this initial phase (e.g., PDF exports, scheduled email delivery). Automated role-based access and self-service distribution can be scoped as a future enhancement.

Deliverables

At the conclusion of the 12-week engagement, you will receive:

Data Integration Platform

- Automated data pipelines pulling from Student Hub and QuickBooks Online
- Scheduled refresh cadence (daily or weekly as required)
- Centralized data warehouse with historical data retention

Three Core Dashboards

- HQ / Royalty Dashboard
- Franchisee Scorecard
- P&L Performance Report
- All dashboards built in selected technology platform (Power BI or React)

Process Documentation

- Data source mapping and transformation logic
- Dashboard navigation and user guide
- Infrastructure architecture overview

Knowledge Transfer

- Walkthrough sessions with key stakeholders
- Admin training for ongoing dashboard maintenance

Project Timeline

We propose a 12-week fixed-duration engagement structured in three phases:

Weeks 1-2: Foundation & Setup

- Requirements validation and refinement
- Infrastructure selection and provisioning
- API connectivity establishment
- Data schema design

Weeks 3-8: Data Integration & Transformation

- API integration development (Student Hub & QuickBooks Online)
- **Delivery Control:** API validation and data completeness testing
- Data pipeline automation
- Transformation logic and calculations
- KPI validation and reconciliation checks
- **Delivery Control:** KPI reconciliation and stakeholder sign-off

Weeks 9-11: Dashboard Development & Testing

- Dashboard design and wireframe design
- **Delivery Control:** Dashboard wireframe approval and stakeholder sign-off
- Report development in selected technology platform
- User acceptance testing with stakeholders
- Iterative refinement based on feedback
- User Acceptance Testing (UAT)
- **Delivery Control:** Final UAT stakeholder sign-off

Week 12: Deployment & Handover

- Production deployment
- Final documentation delivery
- Knowledge transfer sessions
- Hypercare support

Infrastructure Costs (Client Responsibility)

Infrastructure costs will be incurred separately by the client. Below are indicative monthly cost ranges based on industry providers (Azure, AWS, Snowflake, BigQuery):

Option 1: Power BI Platform

Phase 1 (~70 franchises): ~\$1,200/month

Expansion to 500 franchises: ~\$4,500/month

Option 2: Custom React Application

Phase 1 (~70 franchises): ~\$600/month

Expansion to 500 franchises: ~\$2,500/month

Note: Sayer will facilitate infrastructure setup and selection as part of the engagement, but ongoing infrastructure costs are billed directly by the cloud provider.

Working Agreement

Client Responsibilities

To ensure project success, the client agrees to:

- Provide timely access to API credentials for Student Hub and QuickBooks Online
- Provide access to key stakeholders for requirements validation and UAT
- Procure and provide access to selected cloud infrastructure platform
- Respond to data validation questions and reconciliation checks within agreed timelines
- Designate a primary point of contact for project coordination

Sayer Responsibilities

Sayer will:

- Deliver all work remotely unless otherwise mutually agreed
- Provide weekly progress updates and milestone visibility
- Maintain clear communication on any scope adjustments or blockers
- Ensure data architecture is designed for scale and future growth
- Facilitate infrastructure selection and setup

Next Steps

To move forward with this engagement:

1 Confirm technology platform preference
(Power BI vs. React) or schedule a follow-up discussion to evaluate options

3 Review and approve final pricing

2 Validate assumptions
Outlined in the Scope of Work section, particularly regarding QBO consistency across franchises

4 Execute contract and schedule kickoff

We're ready to begin as soon as you are.
